

## **April 2018 HDHQ Construction Small Business Dashboard**

#### Summary

20%

15%

10%

5%

0%

3.6%

Q4

2016

0.4%

Q1

2017

- These charts are based on contracts awarded to date.
- The contractor's goal is to award 20% of total contract dollars to MWS-DVESB firms. Currently, the MWSDVESB Contracted is 19.5%

Multnomah County Health Department Headquarters Construction MWSDVESB Participation J. E. Dunn Construction Contracted and Paid to Date

19.5%

Q2

2018

Participation.

0.0%

Q3

2018

0.0%

Q4

2018

19.5%

Q1

2018

Paid to Date by Quarter

18.3%

Q4

2017

12.4%


Q3

2017

9.2%

Q2

2017

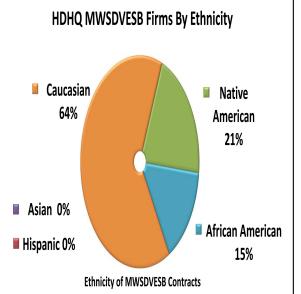

Goal: \$11,464,297 million (20% Participation) based on \$57.3 million total contracted to date. J.E.Dunn Construction

MWSDVESB Participation Project to date, 19.5%. J.E.Dunn


Construction is on track to achieve 20% MWSDVESB

0.0%

Q1

2019

Contract Value

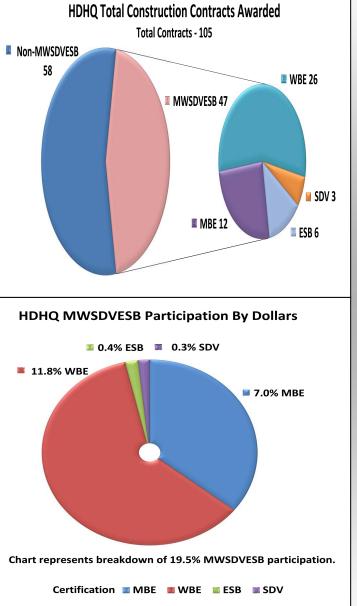

Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran Cumulative Construction Data from 12/31/2016 to 4/30/2018. Produced by Group AGB, Ltd.

0.0%

Q2

2019

0.0%

Q3

2019

-Payments

0.0%


Q4

2019



### **Summary**

- Total Project Apprenticeship to date is 29%
- Project Goal is 20% apprenticeship by trade
- Project minority males participation is 16% and total female participation is 10%

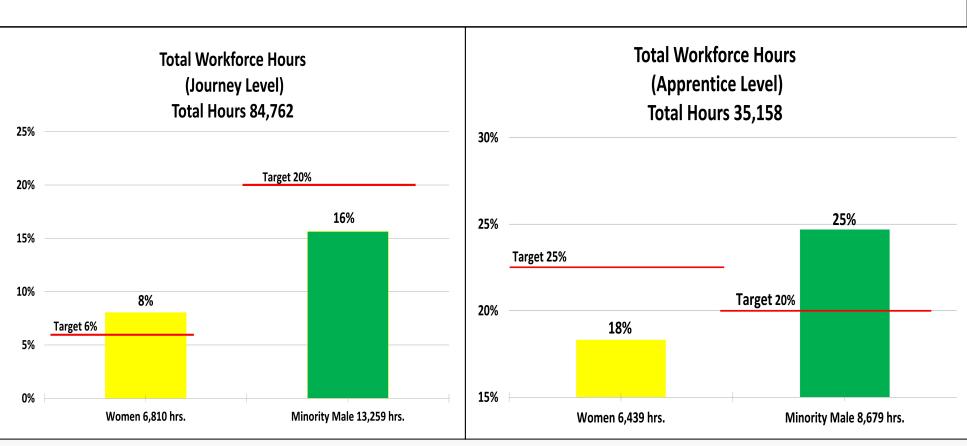


Cumulative Construction Data from 12/31/2016 to 4/30/2018

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.

Produced by Group AGB, Ltd.



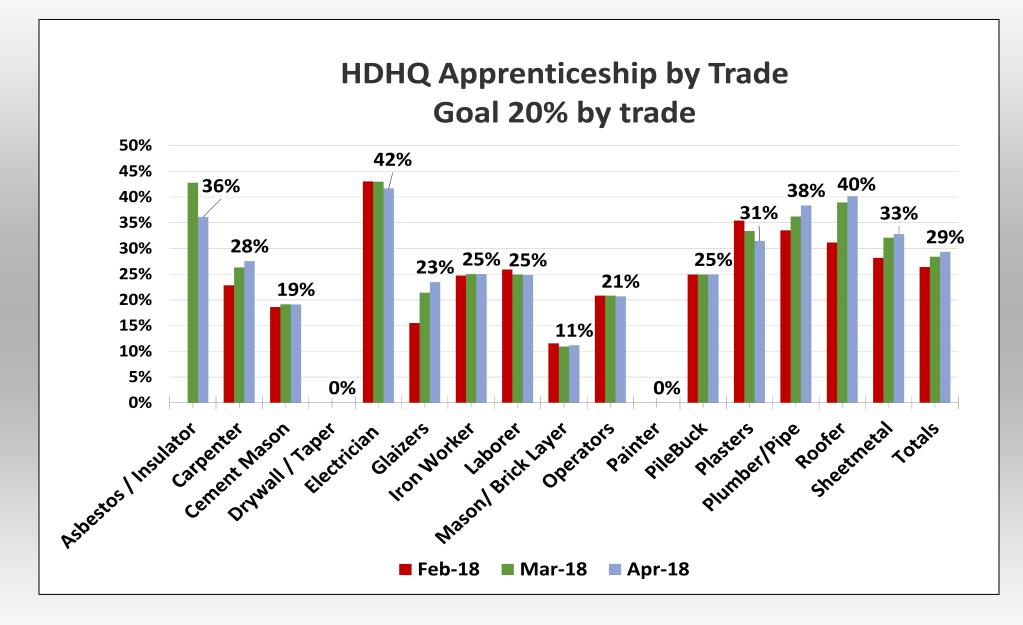


Cumulative Construction Data from 12/31/2016 to 4/30/2018 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



#### **Summary**

- HDHQ GMP of \$65,929,995 approved in June 2017
- J.E. Dunn Construction MWSDVESB Participation is 19.5%
- MWSDVESB contracted excludes yet to be released civil site work, landscaping, and final clean packages





# April 2018 HDHQ Construction MWSDVESB Current vs. Forecast Percentage

