



September 2017 MCCCH Construction Small Business Dashboard


Summary


These charts are based on contracts and dollars awarded to date

The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms. Currently, the MWSDVESB Contracted is 18.6%



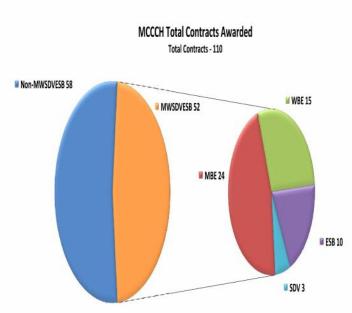

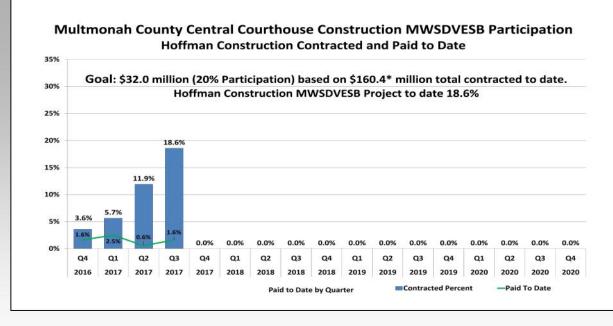




Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran




July 2017 MCCCH Construction Workforce Dashboard

Summary

- Total Project Apprenticeship to date is 23%
- Project Goal is 20% apprenticeship by trade
- Project Total minority participation is 1% and female is 9%

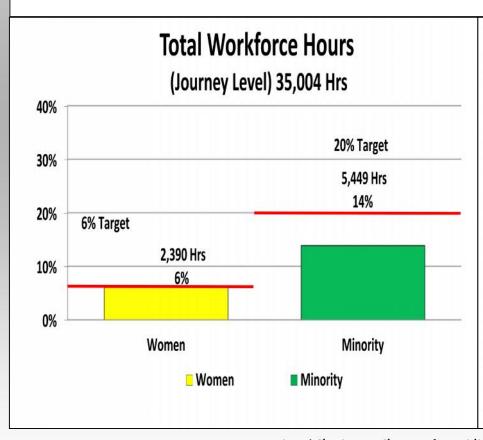


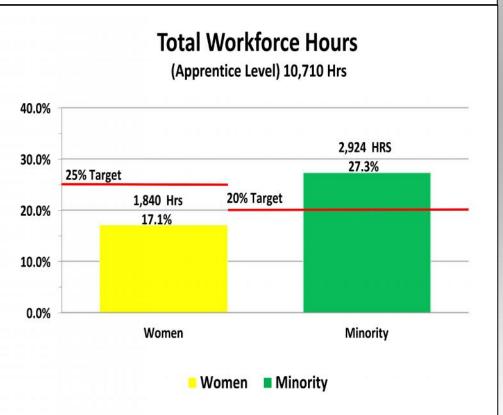





July 2017 MCCCH Construction Workforce Dashboard

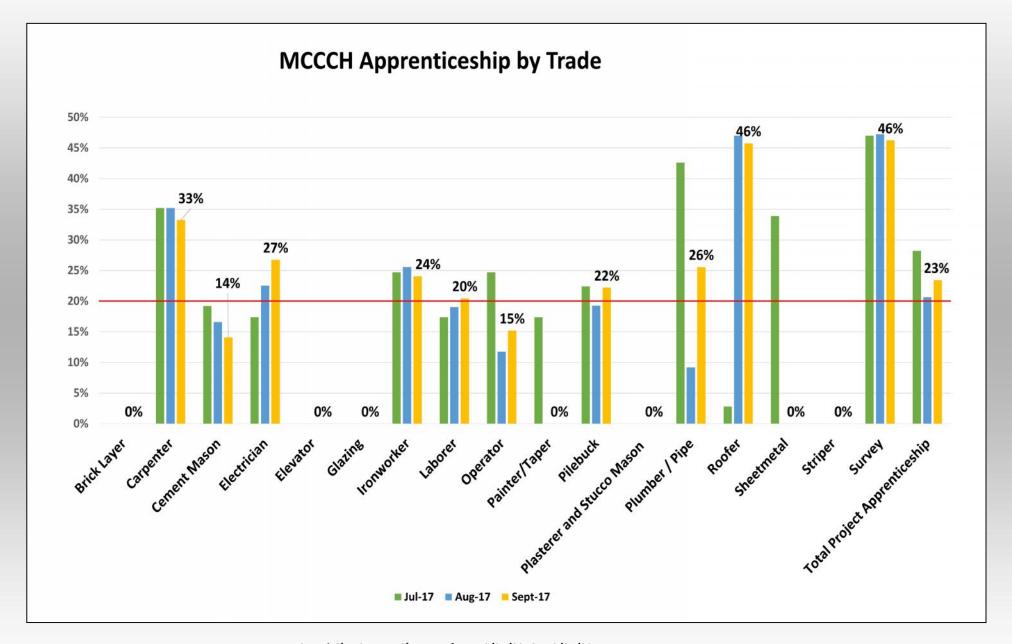







August 2017 MCCCH Construction Workforce Dashboard

Summary-

- Project has achieved 93% of the 20% MWSDVESB goal
- With funding of Trade Partner GMPs, they are moving forward with finalizing MWSDVESB subcontract values
- **Underslab utilities, basement wall Shotcrete, and column rebar activities underway**
- Continuing buyout of Bid Packages 6 and 7

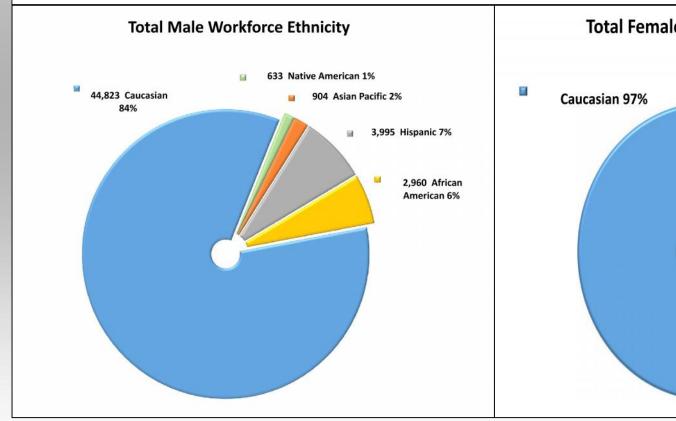

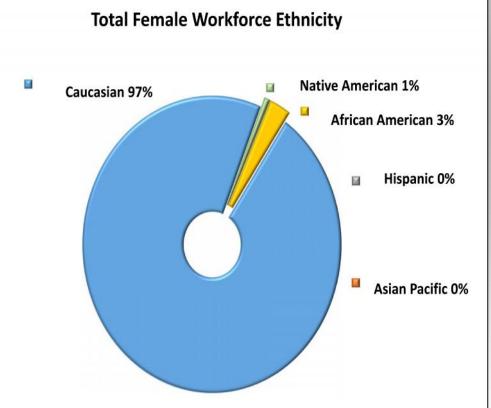





September 2017 MCCCH Construction MWSDVESB Actual vs Forecast Percentage

