

December 2019 MCCCH Construction Small Business Dashboard


Summary

These charts are based on contracts and dollars awarded to date.

The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms.


Currently, MWSDVESB Contracted is 32.7% *

MCCCH MWSDVESB Firms Ethnicity




MCCCH Total Contracts Awarded


Total Contracts - 267



Multnomah County Central Courthouse Construction MWSDVESB Participation Hoffman Construction Contracted and Paid to Date

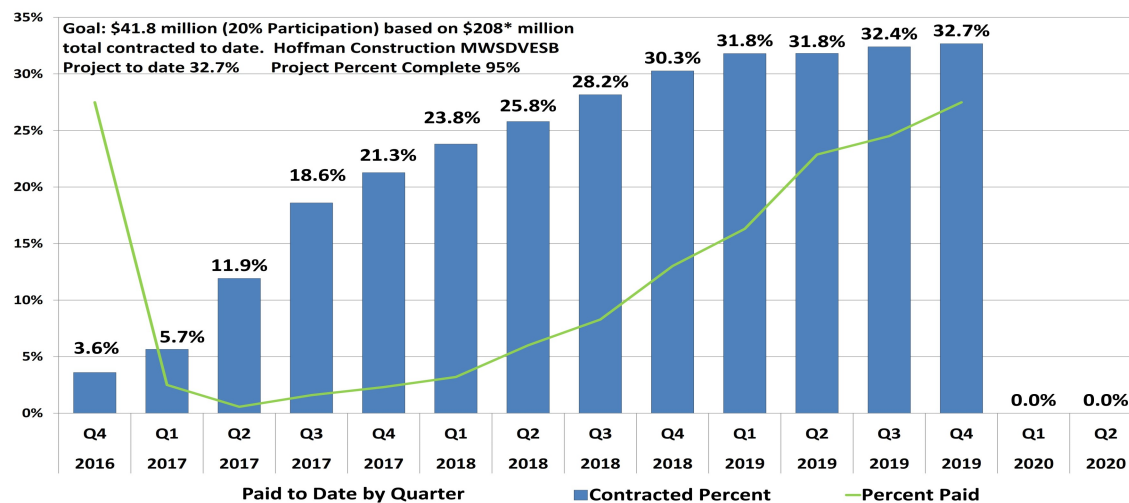


MCCCH MWSDVESB Participation By Dollars



Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran

*Represents adjusted GMP construction value
Cumulative Construction Data from 10/31/2016 to 12/31/2019




December 2019 MCCCH Construction Workforce Dashboard


Project Summary

- Total Project Apprenticeship to date is 30%
- Project Goal is 20% apprenticeship by trade
- Project Total minority male participation is 27.7% and female is 10.3%
- Project Percent Complete 95%

Total Workforce Hours (Journey Level) 856,813 Hrs

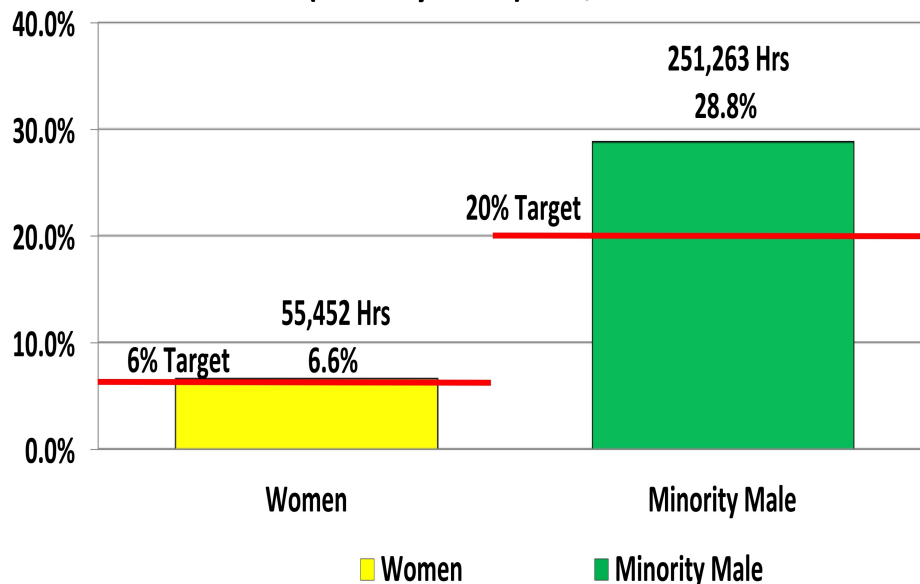

Total Workforce Hours (Apprentice Level) 370,089 Hrs

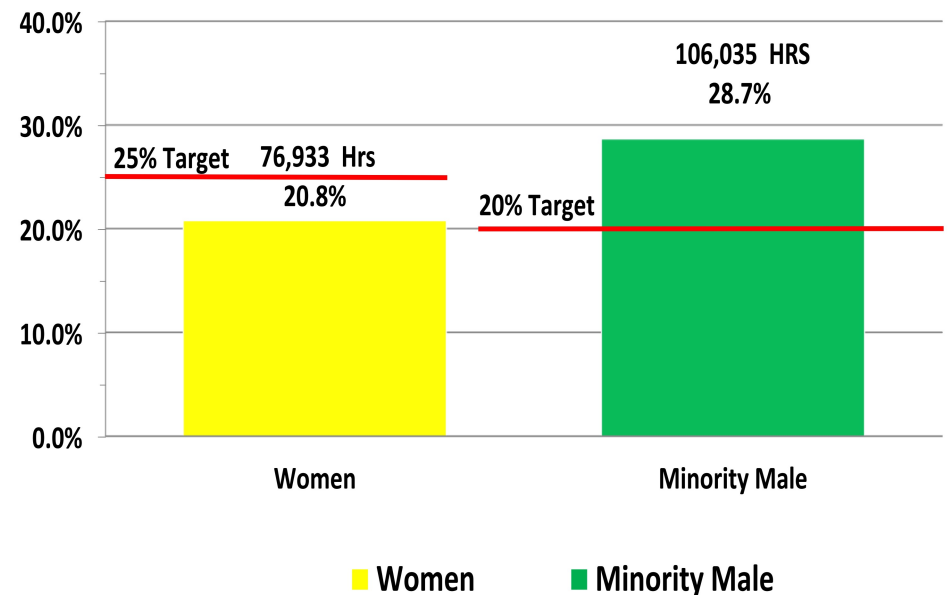

Cumulative Construction Data from 10/31/2016 to 11/30/2019


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



December 2019 MCCCH

Construction Workforce Dashboard

MCCCH Apprenticeship by Trade

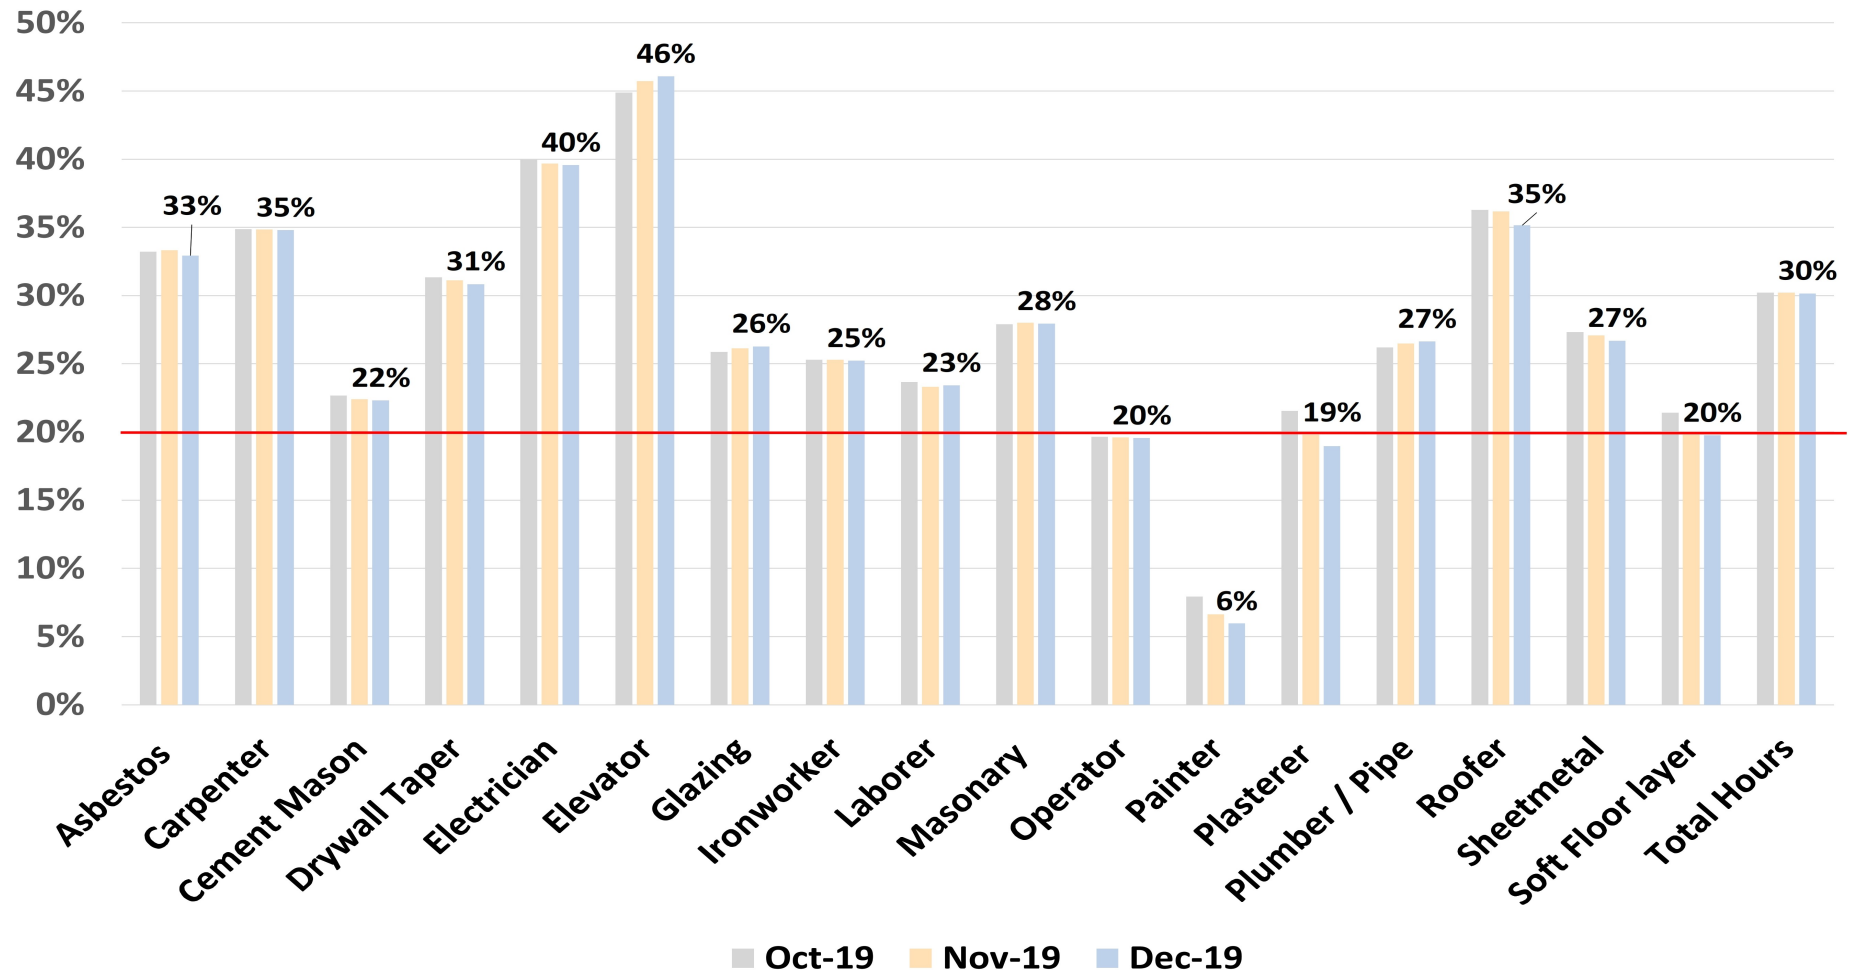

Cumulative Construction Data from 10/31/2016 to 12/31/2019


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



December 2019 MCCCH

Construction Workforce Dashboard

MCCCH Minority Male Journey & Apprenticeship by Trade Hours

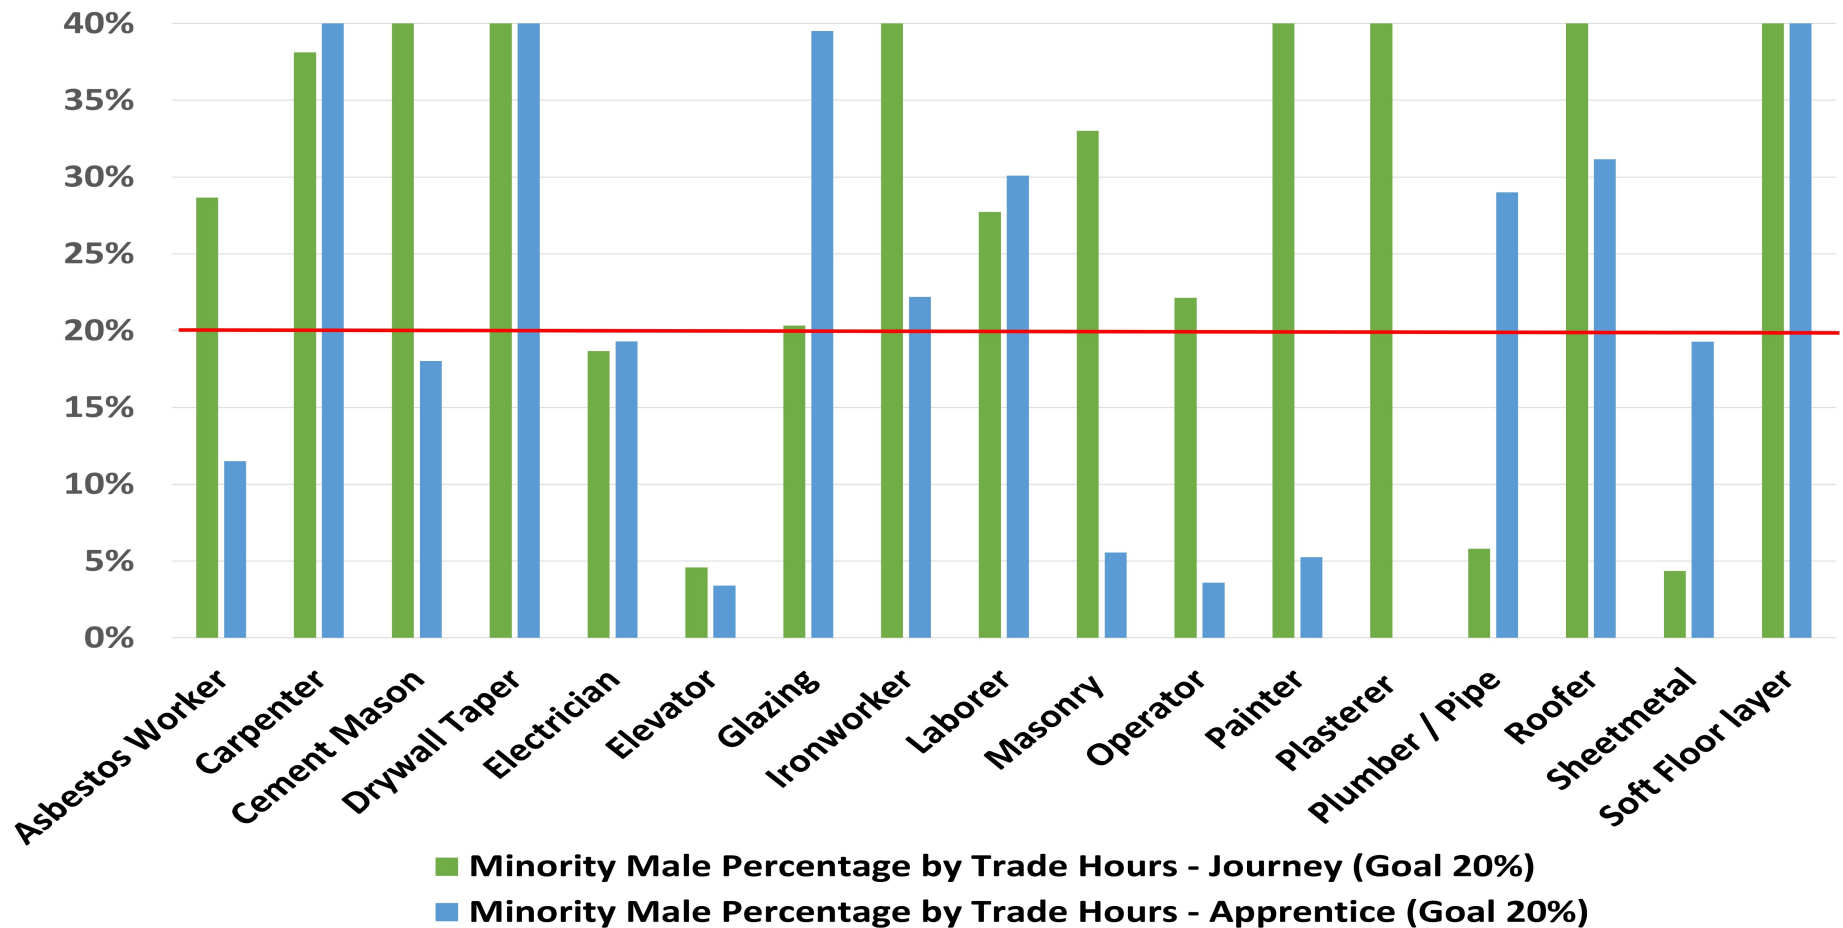


Cumulative Construction Data from 10/31/2016 to 12/31/2019

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.




December 2019 MCCCH Construction Workforce Dashboard

MCCCH Female Journey & Apprenticeship by Trade Hours

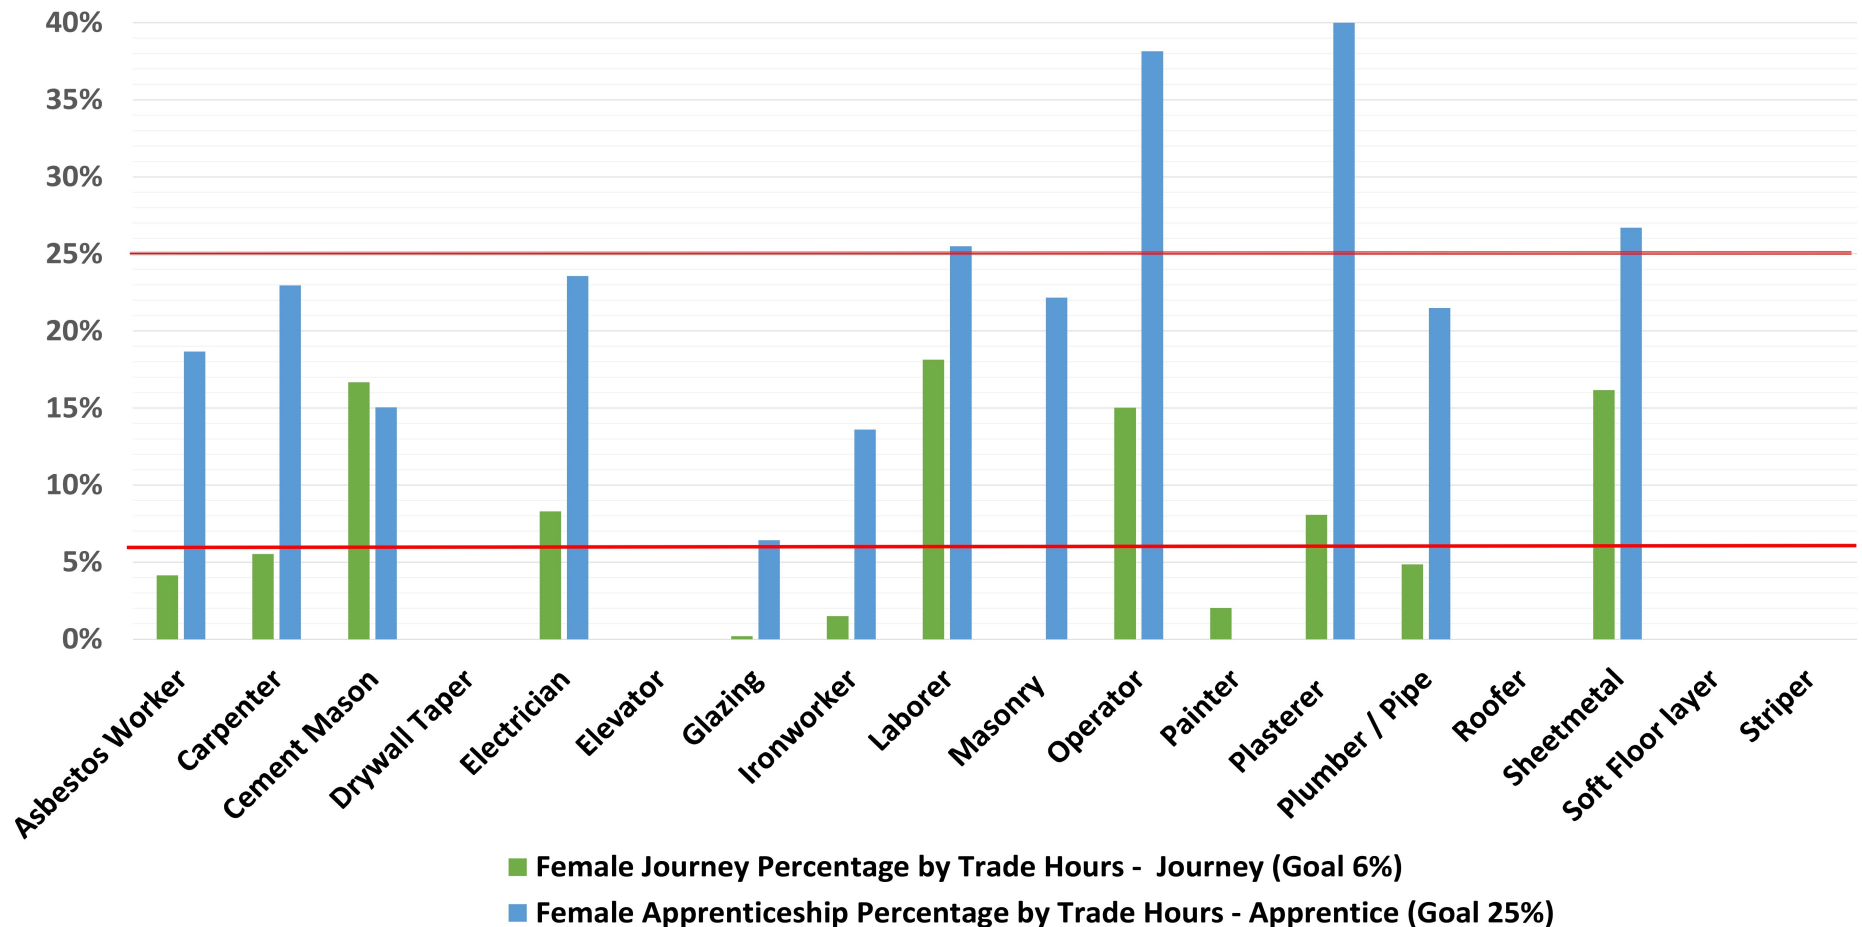

Cumulative Construction Data from 10/31/2016 to 12/31/2019

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.




December 2019 MCCCH Construction Workforce Dashboard


Project Summary—

- 200+ Workers Daily - Consistent Workforce Diversity
- Interior Punchlist Process Underway
- Frontage / Plaza Work Starting
- Major subcontractors are completing scopes and reducing crews
- Percentage Complete 95%

Total Male Workforce By Ethnicity

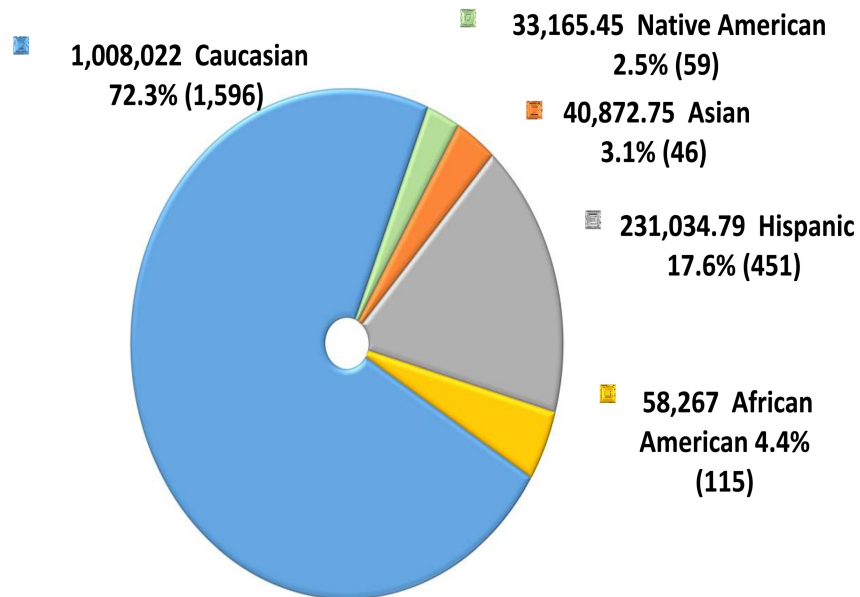

Total Female Workforce Ethnicity

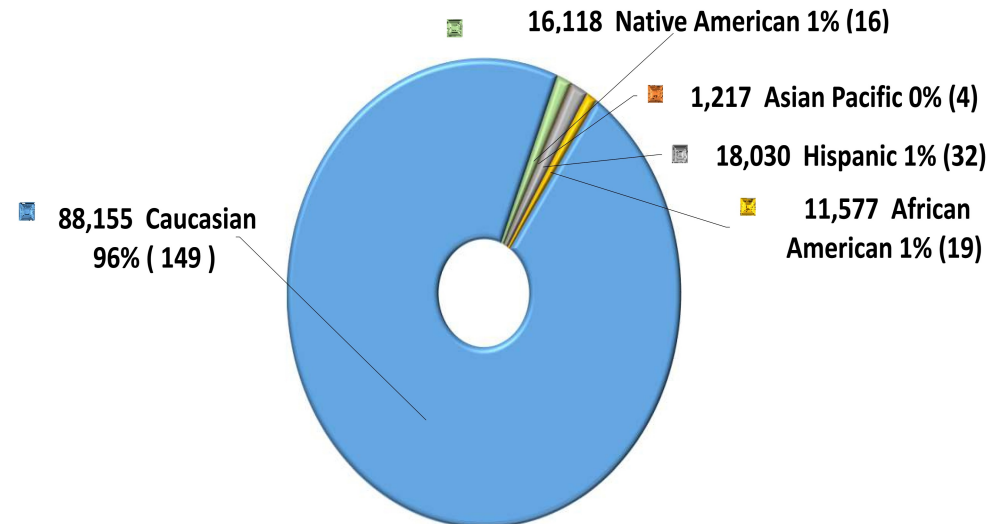




December 2019 MCCCH Construction

MWSDVESB Actual vs Forecast Percentage

Project Percent Complete 95%

MCCCH MWSDVESB Current Percentage 32.7% - December 2019

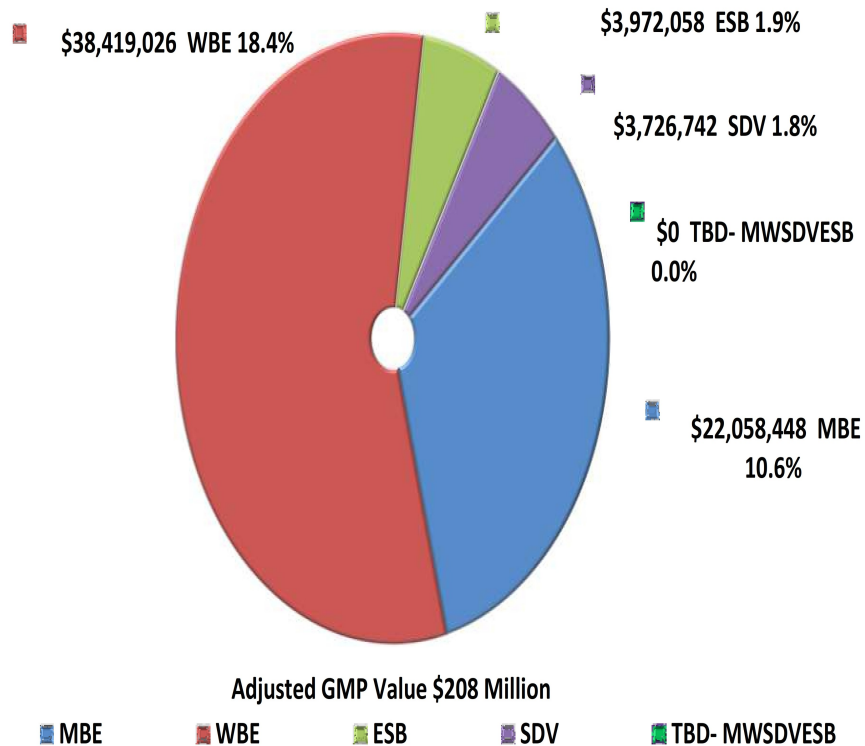

MCCCH MWSDVESB Forecast Percentage 31.4% - June 2020

