

# January 2020 MCCCH

## Construction Small Business Dashboard


### Summary

These charts are based on contracts and dollars awarded to date.

The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms.


Currently, MWSDVESB Contracted is 33.3% \*

### MCCCH MWSDVESB Firms Ethnicity

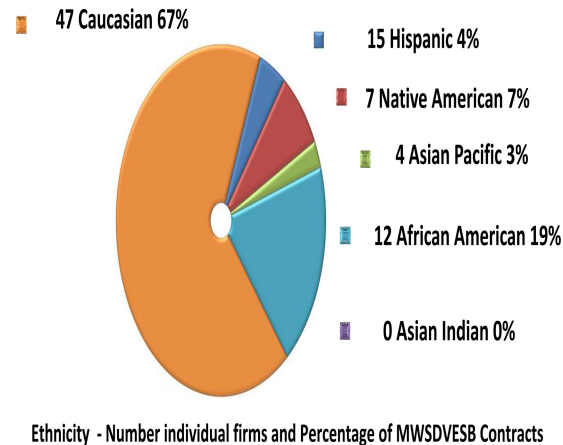


### MCCCH Total Contracts Awarded

Total Contracts - 267

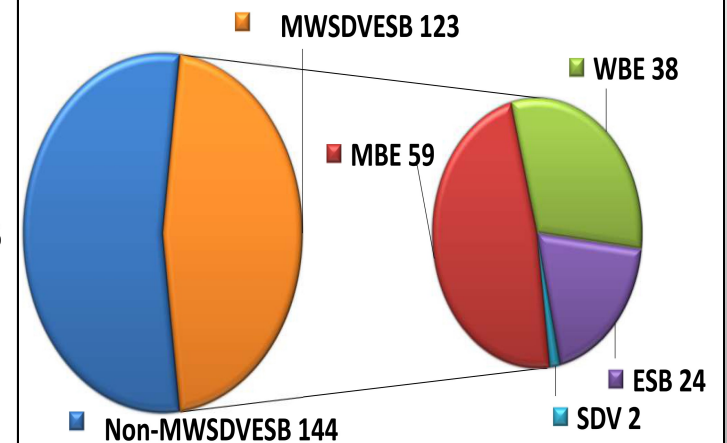


### Multnomah County Central Courthouse Construction MWSDVESB Participation

Hoffman Construction Contracted and Paid to Date

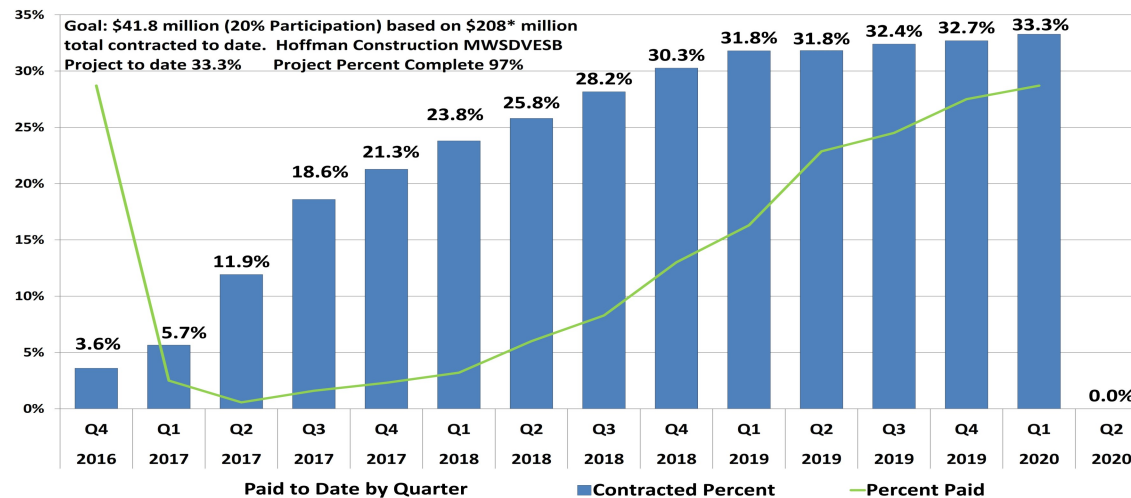


### MCCCH MWSDVESB Participation By Dollars

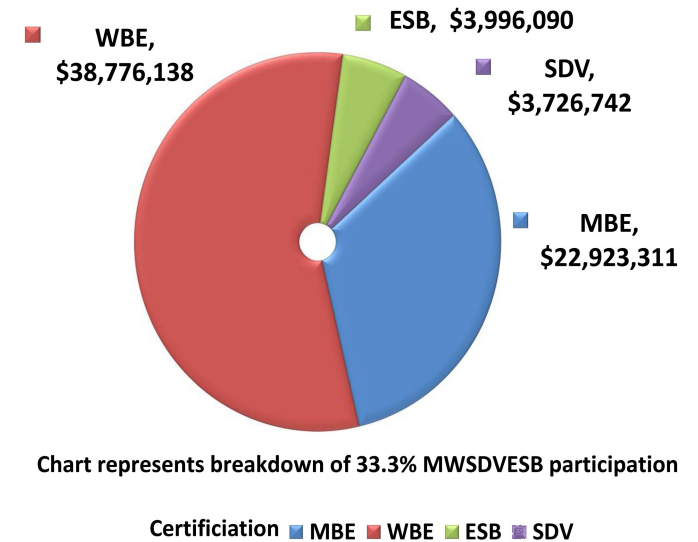

Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran

\*Represents adjusted GMP construction value  
Cumulative Construction Data from 10/31/2016 to 1/31/2020




# January 2020 MCCCH Construction Workforce Dashboard


## Project Summary

- Total Project Apprenticeship to date is 30%
- Project Goal is 20% apprenticeship by trade
- Project Total minority male participation is 27.9% and female is 10.3%
- Project Percent Complete 97%

### Total Workforce Hours (Journey Level) 897,015 Hrs

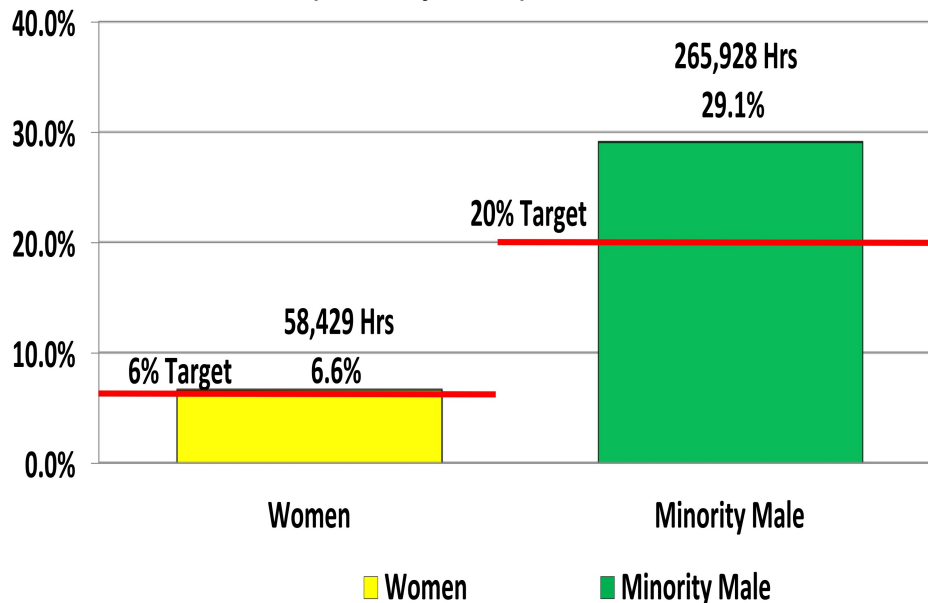

### Total Workforce Hours (Apprentice Level) 385,491 Hrs

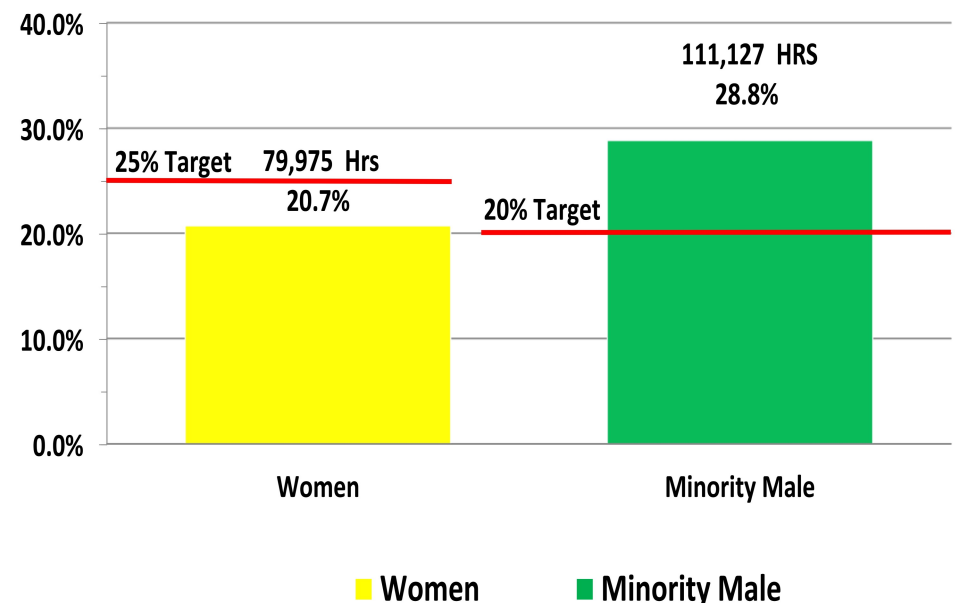

Cumulative Construction Data from 10/31/2016 to 1/31/2020


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



# January 2020 MCCCH

## Construction Workforce Dashboard

### MCCCH Apprenticeship by Trade

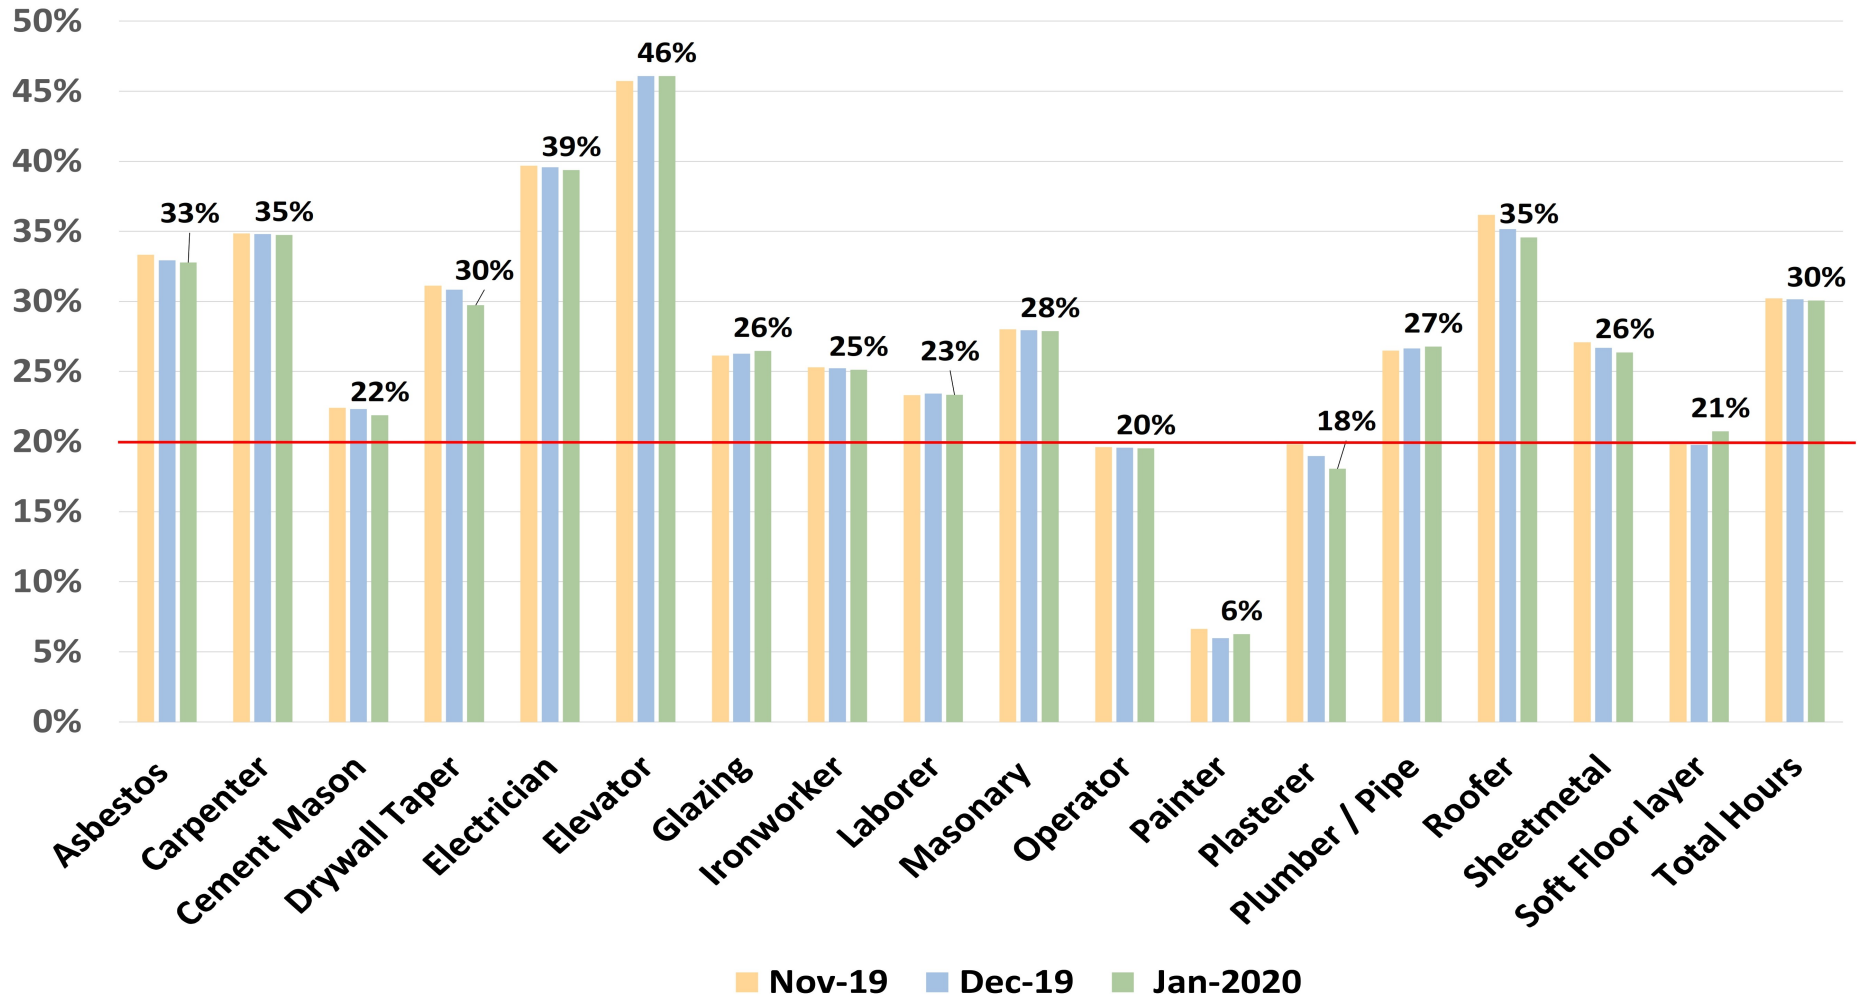

Cumulative Construction Data from 10/31/2016 to 1/31/2020


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



# January 2020 MCCCH

## Construction Workforce Dashboard

### MCCCH Minority Male Journey & Apprenticeship by Trade Hours

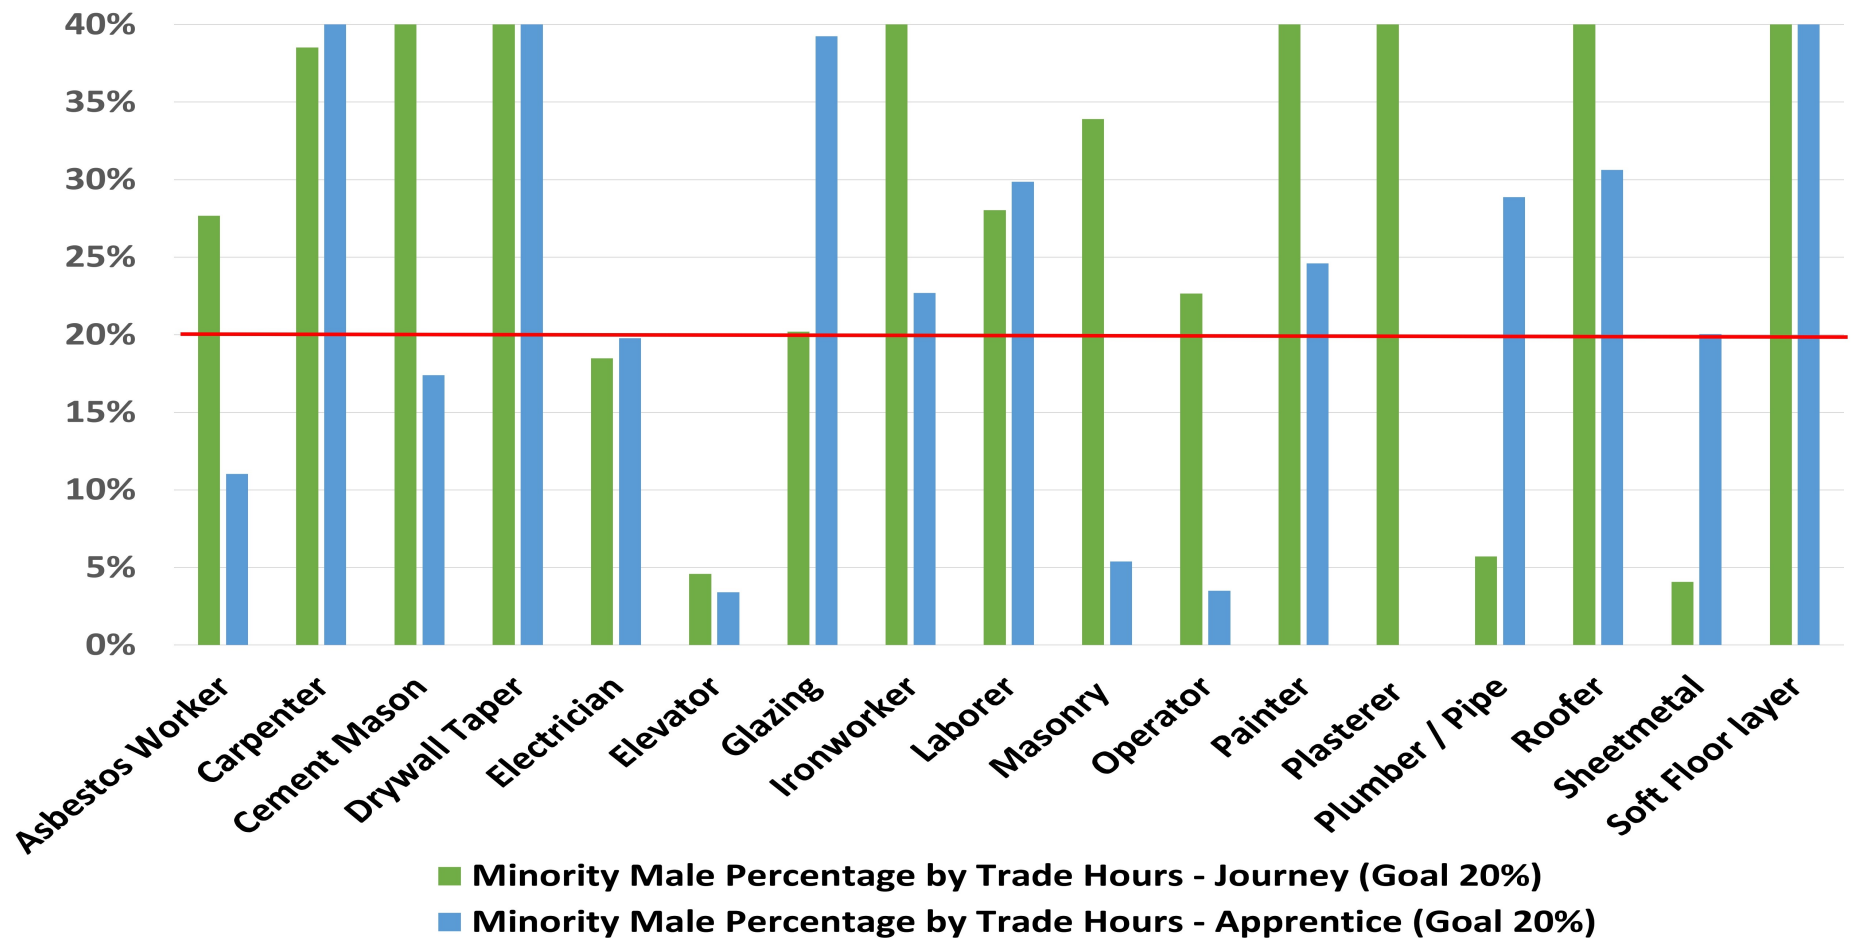

Cumulative Construction Data from 10/31/2016 to 1/31/2020


WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



# January 2020 MCCCH


## Construction Workforce Dashboard

MCCCH Female Journey & Apprenticeship by Trade Hours

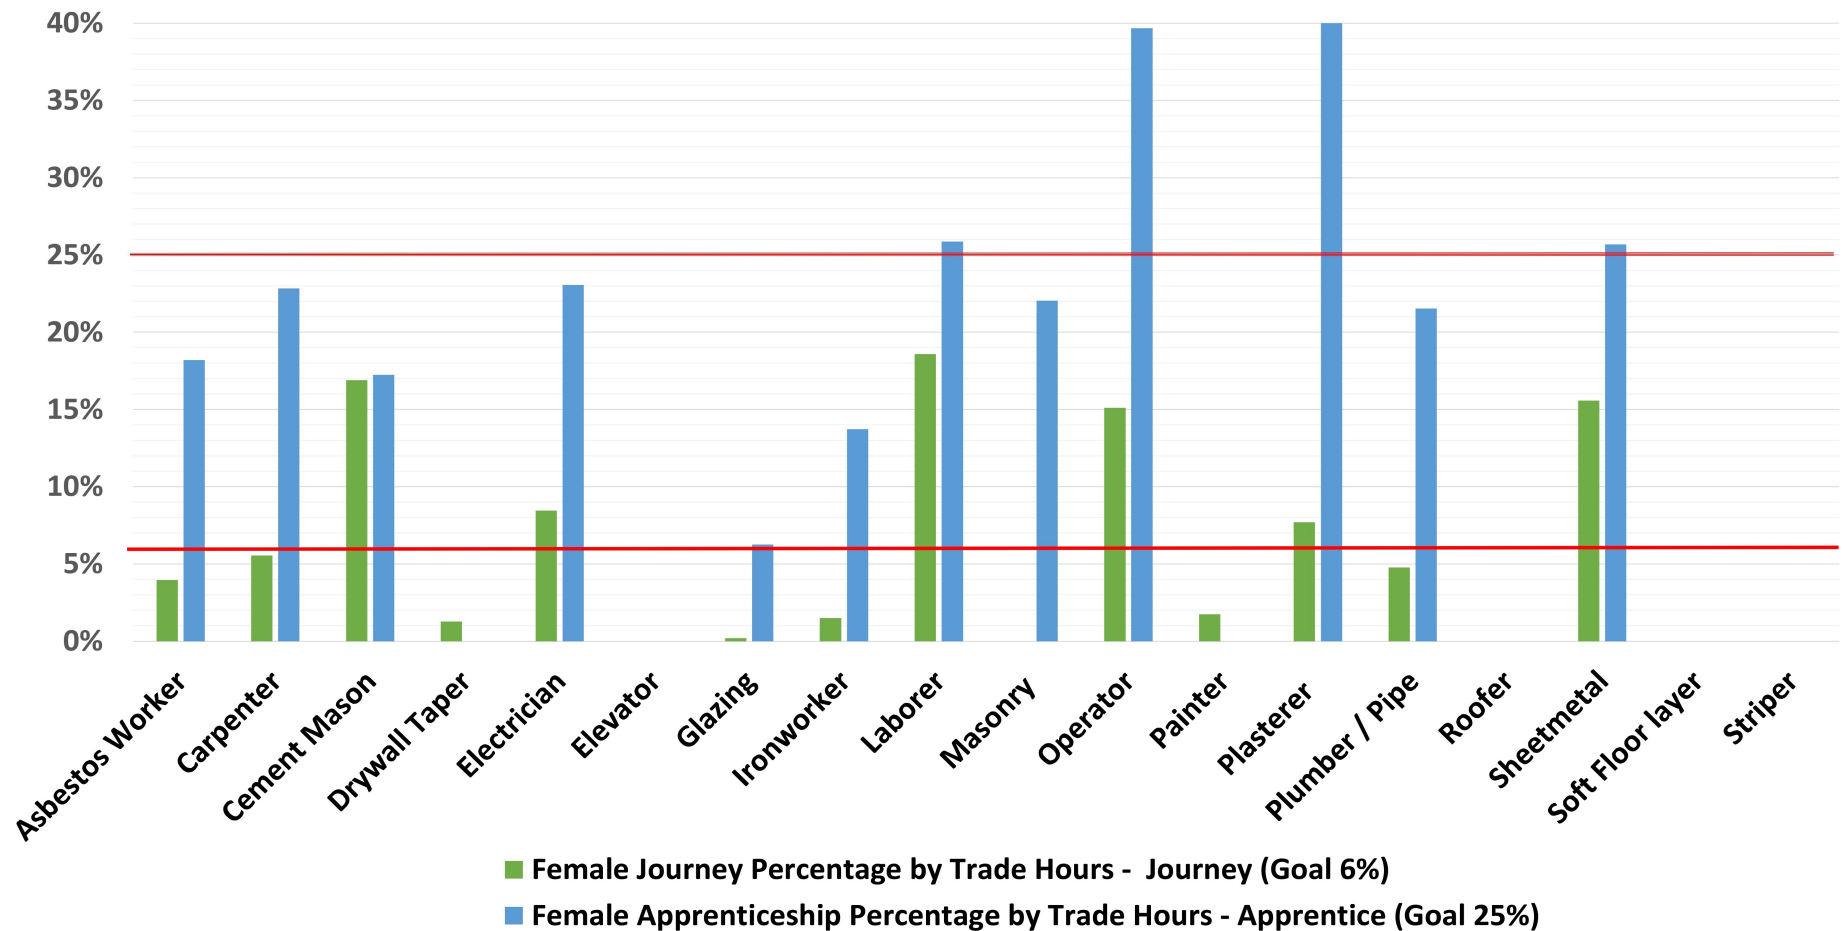

Cumulative Construction Data from 10/31/2016 to 1/31/2020

WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.




# January 2020 MCCCH Construction Workforce Dashboard


## Project Summary—

- 150+ Workers Daily - Consistent Workforce Diversity
- Interior Punchlist Process Underway
- Frontage / Plaza Work Starting
- Major subcontractors are completing scopes and reducing crews
- Percentage Complete 97%

Total Male Workforce By Ethnicity

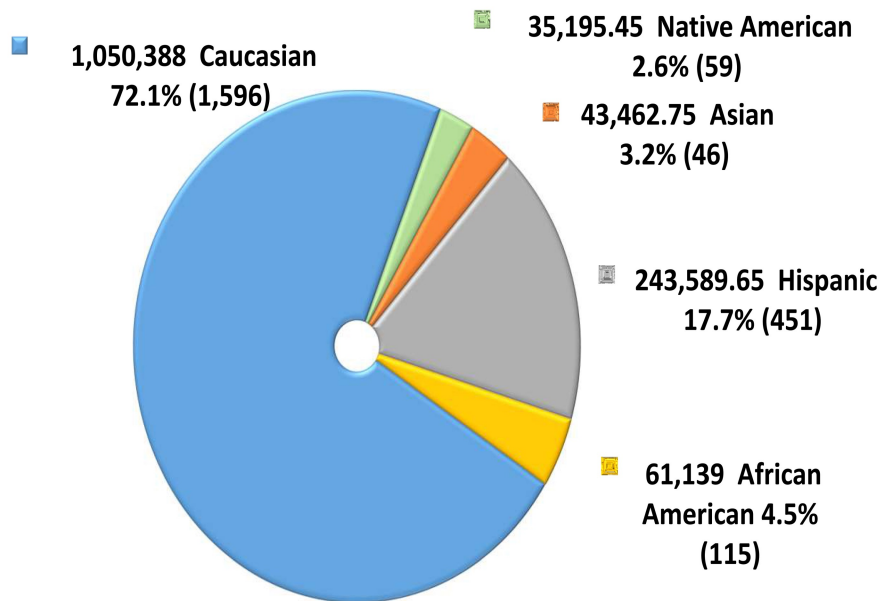

Total Female Workforce Ethnicity

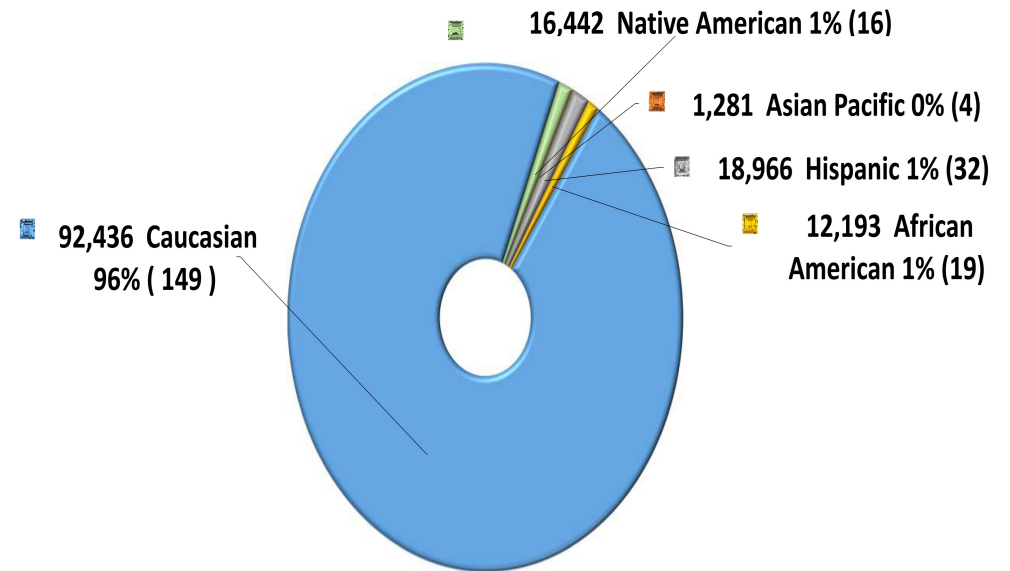




# January 2020 MCCCH Construction

## MWSDVESB Actual vs Forecast Percentage

### Project Percent Complete 97%

**MCCCH MWSDVESB Current Percentage 33.3% - January 2020**

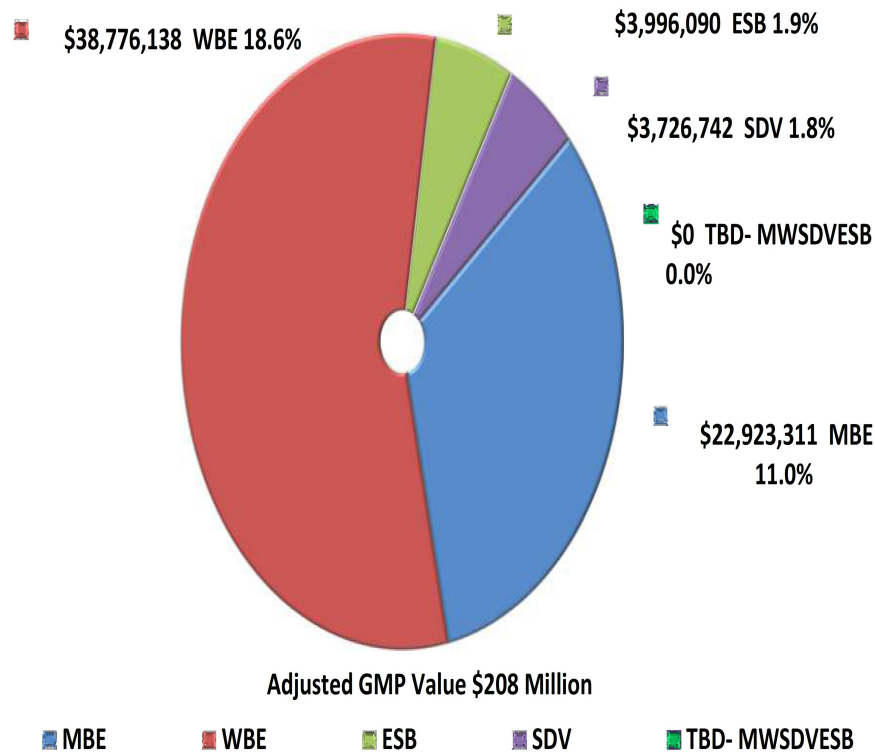

**MCCCH MWSDVESB Forecast Percentage 31.4% - June 2020**

