




# June 2017 HDHQ Construction Small Business Dashboard

## Summary

These charts are based on contracts awarded through June 2017.


The contractor's goal is to award 20% of total contract dollars to MWSDVESB firms. Currently, the MWSDVESB Contracted is 5.7% and the MWSDVESB Paid is 0.2%.

HDHQ MWSDVESB Firms Ethnicity




Data collected from required project forms. Ethnicity of MWSDVESB contracts


HDHQ Total Construction Contracts Awarded

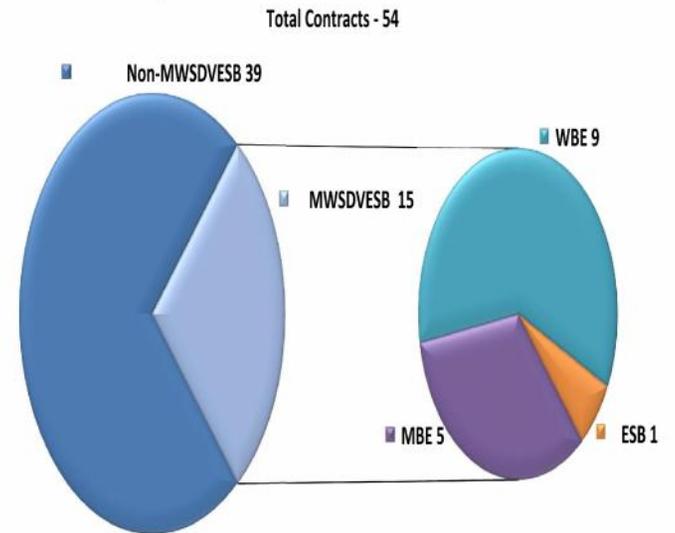

Multnomah County Health Department Headquarters Construction MWSDVESB Participation

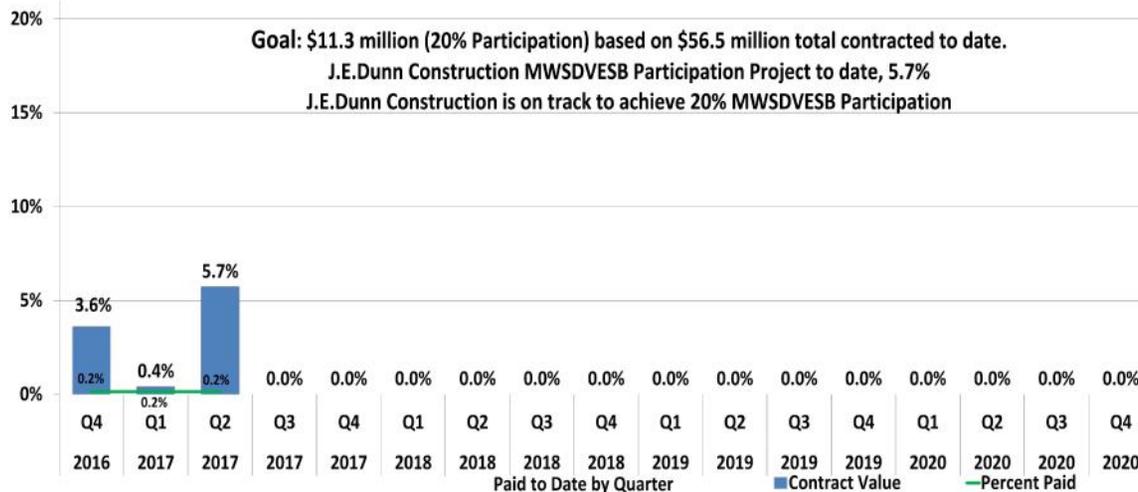

HDHQ MWSDVESB Participation by Dollars

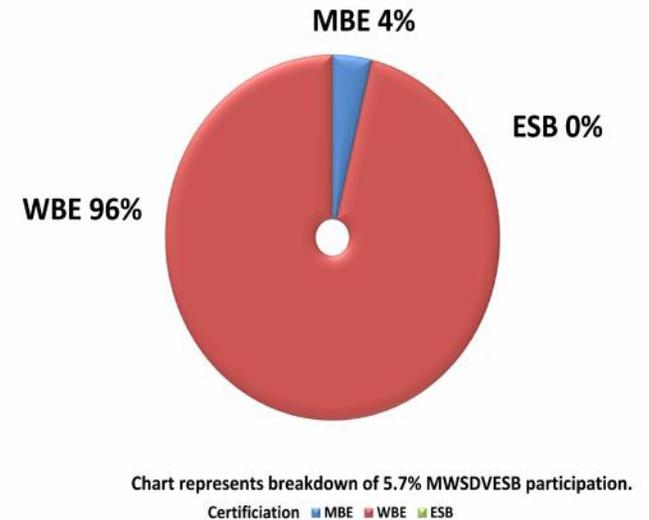

Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran

Cumulative Construction Data from 12/31/2016 to 6/30/2017. Produced by Group AGB, Ltd.



# June 2017 HDHQ Construction Workforce Dashboard


## Summary

- )] Total Project Apprenticeship to date is 19%
- )] Project Goal is 20% apprenticeship by trade
- )] Project minority participation is 20% and female is 12%

### Total Workforce Hours

(Journey Level)


Total Hours 10,718

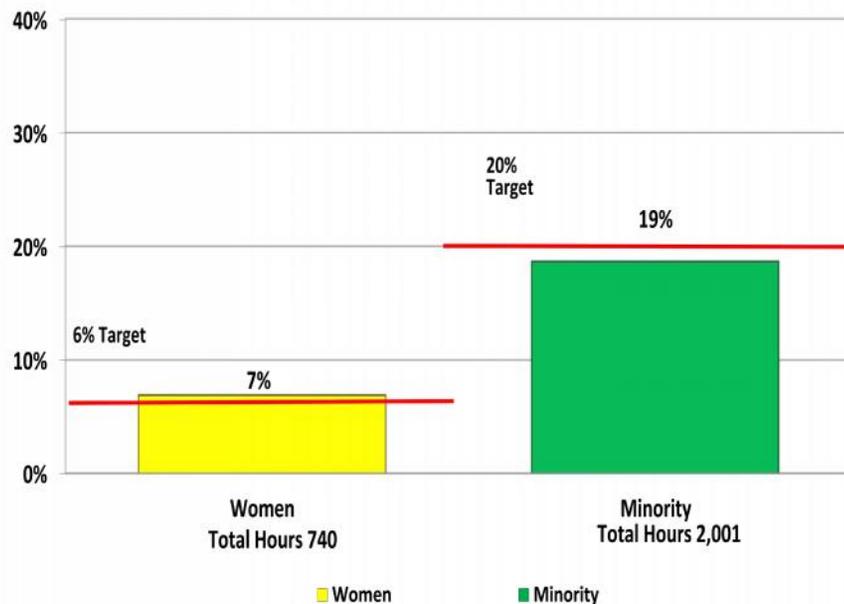

### Total Workforce Hours

(Apprentice Level)

Total Hours 2,495

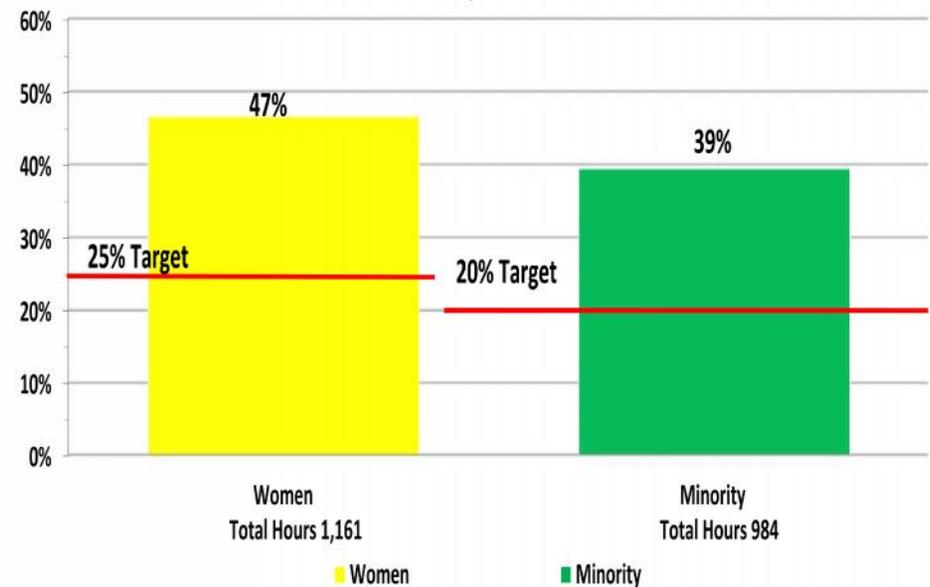

Cumulative Construction Data from 12/31/2016 to 6/30/2017


WTHP Participation for minorities and women for apprentices and journey level in accordance with the PLA.

Produced by Group AGB, Ltd.



# June 2017 HDHQ Construction Workforce Dashboard

## HDHQ Apprenticeship by Trade

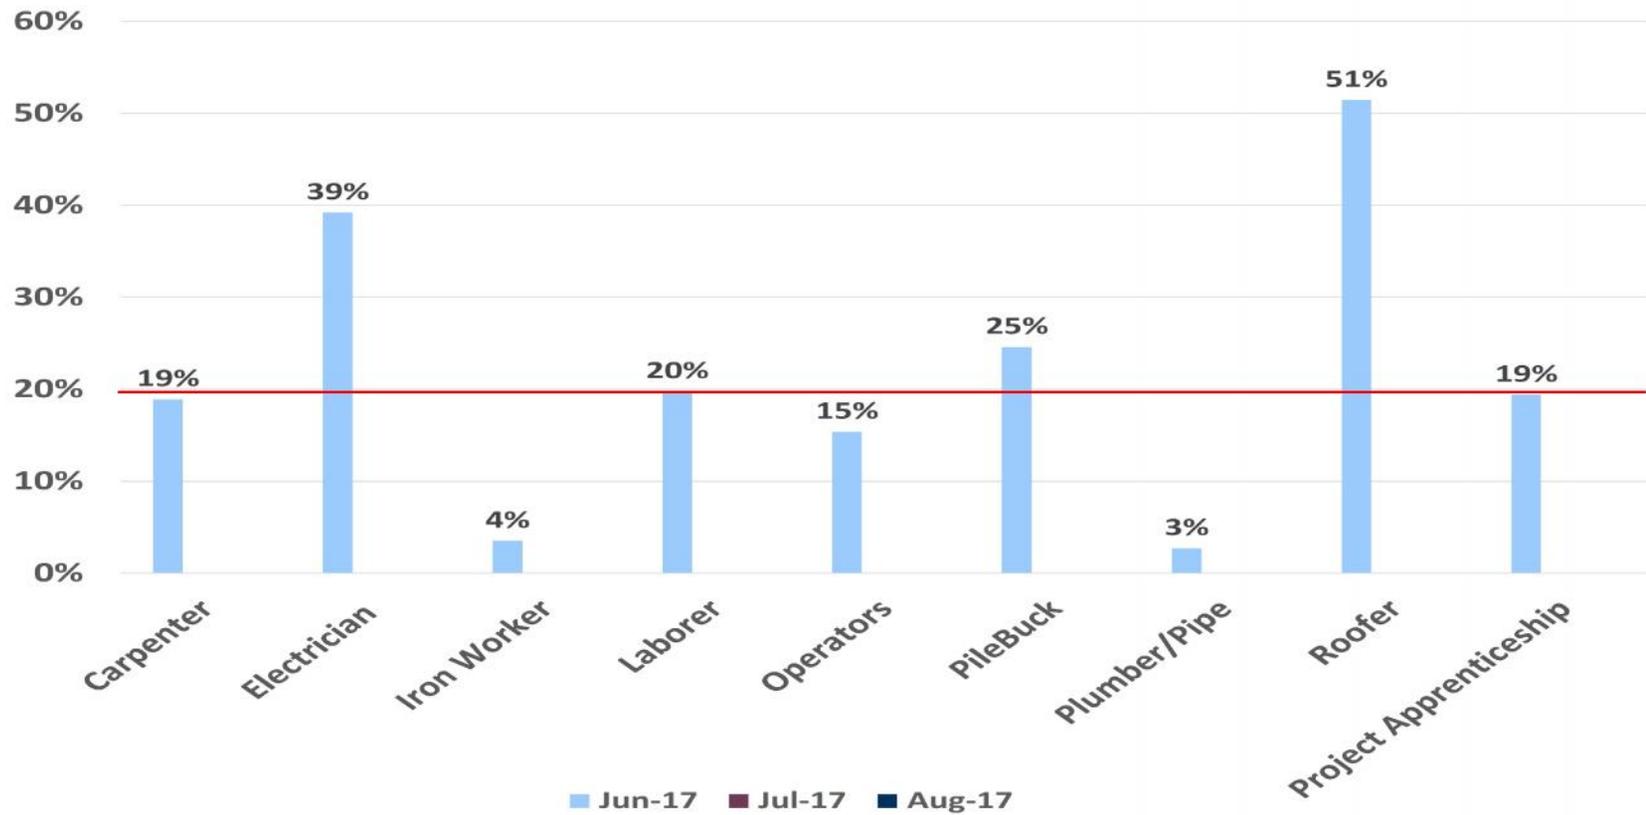

Cumulative Construction Data from 12/31/2016 to 6/30/2017  
WTHP Participation for minorities and women for apprentices and journey level in accordance with the PLA.  
Produced by Group AGB, Ltd.




# June 2017 HDHQ Construction Workforce Dashboard

## Summary

- HDHQ GMP of \$65,929,995 approved in June 2017
- MWSDVESB contracted and WFTH percentages represents mostly pre-construction and foundation work

### Total Male Workforce Ethnicity



### Total Female Workforce Ethnicity

