




August 2018 MCCCH Construction Small Business Dashboard


Summary

- These charts are based on contracts and dollars awarded to date.
- The contractor's goal is to award 20% of total contract dollars to MWS-DVESB firms. Currently, MWSDVESB Contracted is 27.9% *

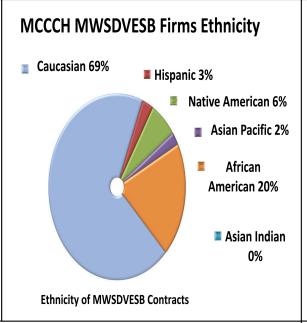

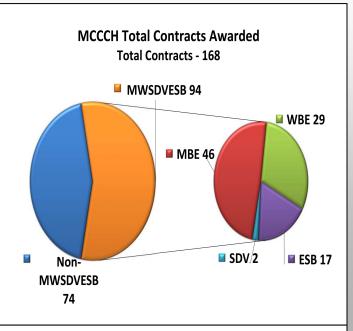

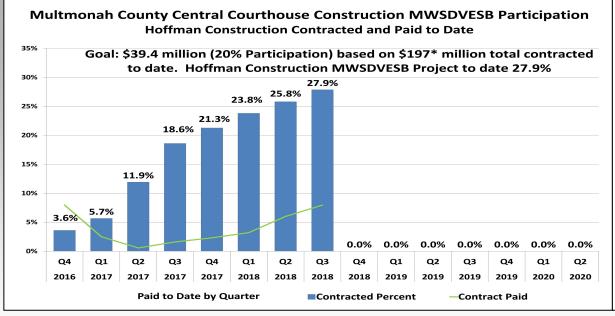

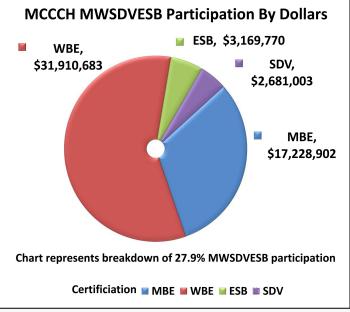


Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran




August 2018 MCCCH Construction Workforce Dashboard

Project Summary

- Total Project Apprenticeship to date is 28.2%
- Project Goal is 20% apprenticeship by trade
- Project Total minority participation is 19.8% and female is 9.8%

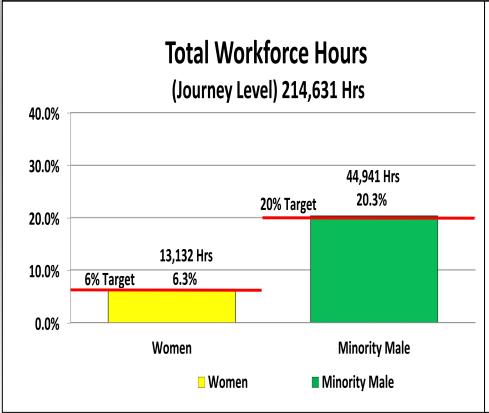


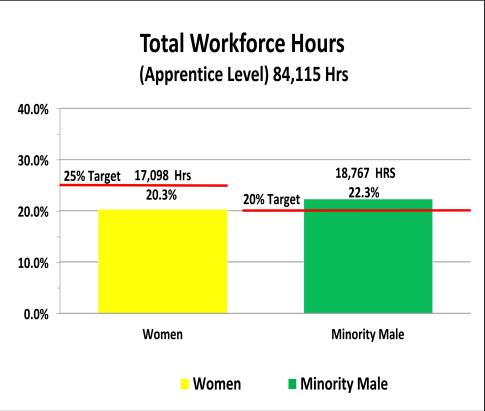

Cumulative Construction Data from 10/31/2016 to 8/31/2018 WTHP Participation for minority men and all women for apprentice and journey levels in accordance with the PLA.



August 2018 MCCCH Construction Workforce Dashboard

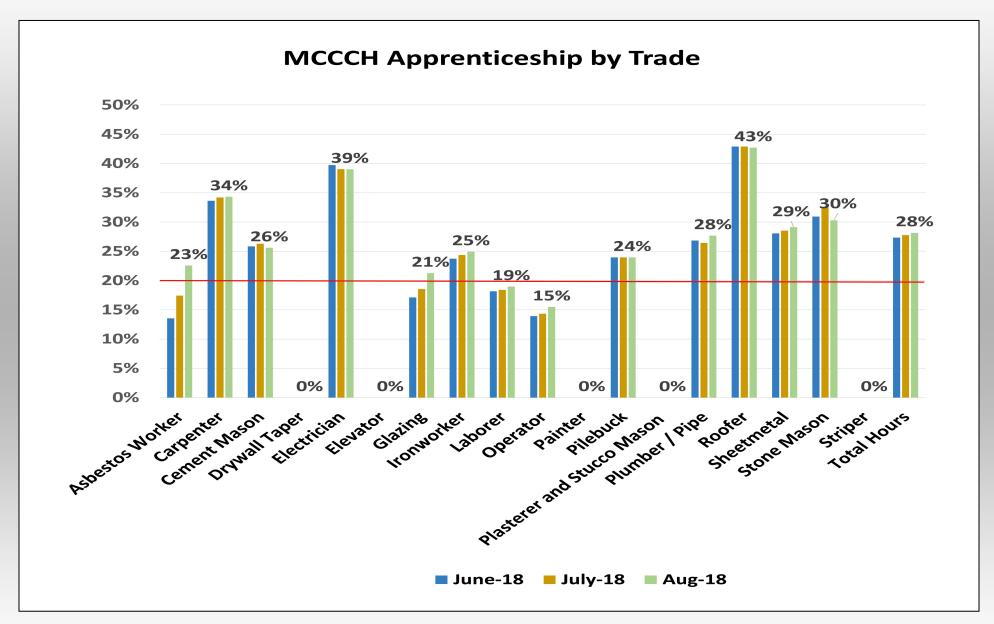



August 2018 MCCCH Construction Workforce Dashboard

Project Summary-

- Exceeding MWSDVESB and overall apprenticeship goal
- Majority of subs have mobilized a few still to onboard
- 250+ workers daily diversity continues to increase
- Focused support on smaller subs who struggle with timely reporting and tracking ratios

