




### June 2018 HDHQ Construction Small Business Dashboard


#### Summary

- These charts are based on contracts awarded to date.
- The contractor's goal is to award 20% of total contract dollars to MWS-DVESB firms. Currently, the MWSDVESB Contracted is 22.4%

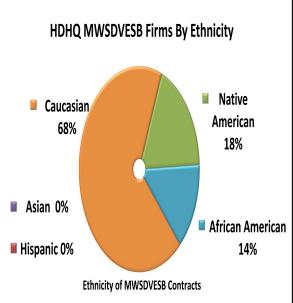

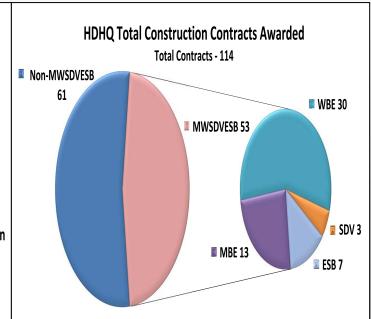

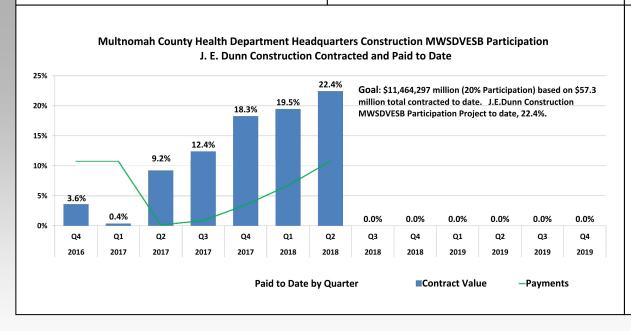

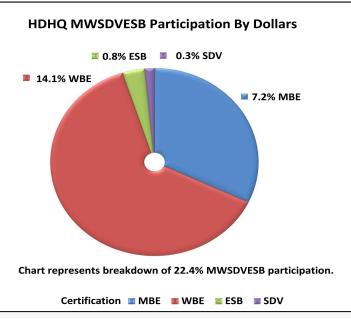


Glossary: MBE—Minority-Owned Business, WBE—Women-Owned Business, ESB—Emerging Small Business, SDV - Service Disabled Veteran Cumulative Construction Data from 12/31/2016 to 6/30/2018. Produced by Group AGB, Ltd.




## June 2018 HDHQ Construction Workforce Dashboard

#### **Summary**


- Total Project Apprenticeship to date is 30%
- Project Goal is 20% apprenticeship by trade
- Project minority males participation is 19.8% and total female participation is 9.9%

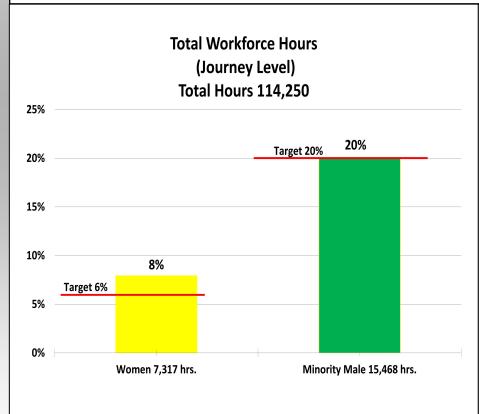

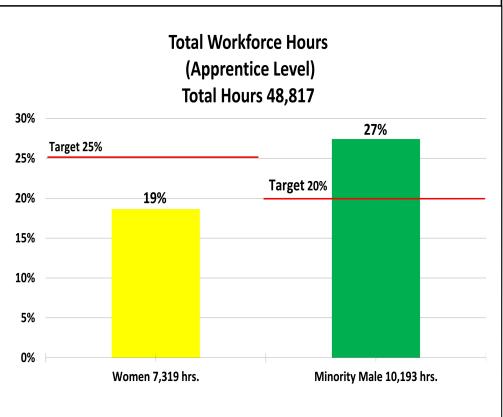



## June 2018 HDHQ Construction Workforce Dashboard

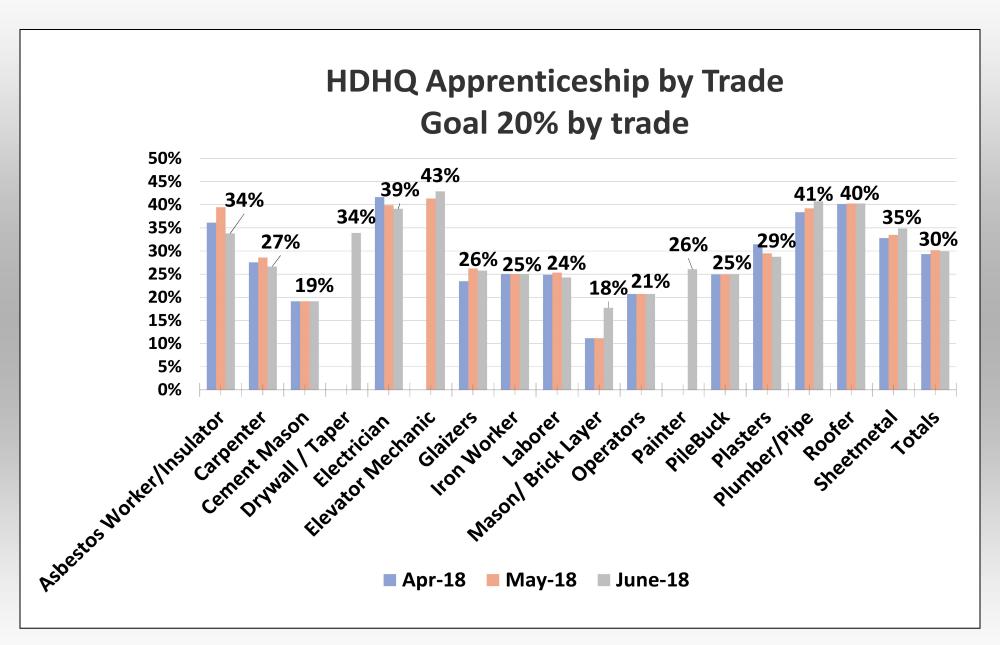




## June 2018 HDHQ Construction Workforce Dashboard

#### **Summary**

- HDHQ GMP of \$65,929,995 approved in June 2017
- J.E. Dunn Construction MWSDVESB participation exceeded 20% goal, currently at 22.4%
- MWSDVESB contracted excludes yet to be released civil site work, landscaping, and final clean packages

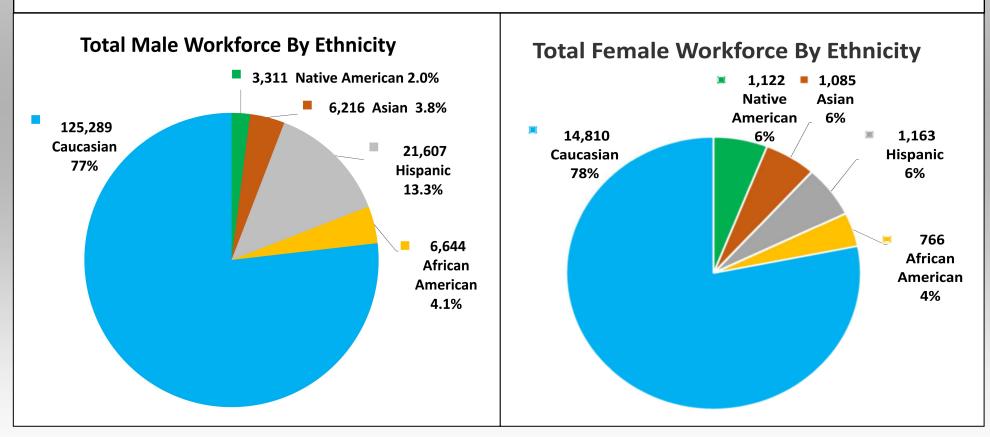



# June 2018 HDHQ Construction MWSDVESB Current vs. Forecast Percentage

